



AMERICAN INTERNATIONAL UNIVERSITY–BANGLADESH (AIUB)

**Department of Computer Science
Faculty of Science & Technology (FST)**

Fall 2024-25

Section: H, Group: 01

PROJECT TITLE

**Virtual Classroom Platform: An Interactive, Accessible, and Engaging Online
Learning Environment**


Supervised By TONNY SHEKHA KAR

Submitted By

Group Members

SN	Name	ID
1	AFNAN BIN ISLAM NAHIN	22-49350-3
2	AMAN ULLAH	22-49345-3
3	HRITTIK BHATTACHARJEE	21-44650-1
4	MD. HACHIBUR RAHMAN	22-46426-1
5	WALID BIN KHALED	22-46101-1


Work Breakdown Structure

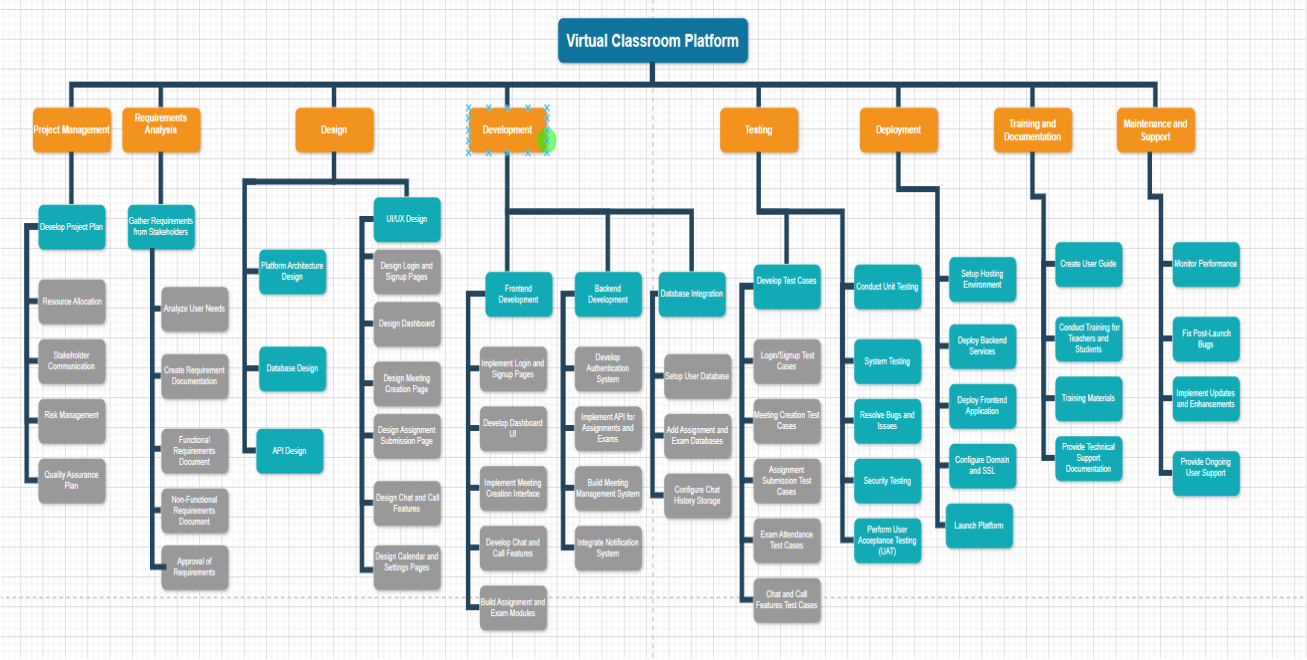

Gantt Chart

		Name	Duration	Start	Finish	Predecessors
1	✖	Virtual Classroom Platform	87 days	10/24/24 8:00 AM	2/21/25 5:00 PM	
2		Project Management	14 days	10/24/24 8:00 AM	11/12/24 5:00 PM	
3		Develop Project Plan	3 days	10/24/24 8:00 AM	10/28/24 5:00 PM	
4		Resource Allocation	4 days	10/29/24 8:00 AM	11/1/24 5:00 PM	3
5		Stakeholder Communication	4 days	11/4/24 8:00 AM	11/7/24 5:00 PM	4
6		Risk Management	3 days	11/4/24 8:00 AM	11/6/24 5:00 PM	4
7		Quality Assurance Plan	4 days	11/7/24 8:00 AM	11/12/24 5:00 PM	6
8		Requirements Analysis	15 days	11/13/24 8:00 AM	12/3/24 5:00 PM	2
9		Gather Requirements from Stakeholders	3 days	11/13/24 8:00 AM	11/15/24 5:00 PM	
10		Analyze User Needs	4 days	11/18/24 8:00 AM	11/21/24 5:00 PM	9
11		Create Requirement Documents	2 days	11/22/24 8:00 AM	11/25/24 5:00 PM	10
12		Functional Requirements	2 days	11/26/24 8:00 AM	11/27/24 5:00 PM	11
13		Non-Functional Requirements	2 days	11/28/24 8:00 AM	11/29/24 5:00 PM	12
14		Approval of Requirements	2 days	12/2/24 8:00 AM	12/3/24 5:00 PM	13
15		Design	10 days	12/4/24 8:00 AM	12/17/24 5:00 PM	8
16		Platform Architecture Design	2 days	12/4/24 8:00 AM	12/5/24 5:00 PM	
17		Class diagram	3 days	12/6/24 8:00 AM	12/10/24 5:00 PM	16
18		ER-diagram	2 days	12/6/24 8:00 AM	12/9/24 5:00 PM	16
19		sequence diagram	3 days	12/6/24 8:00 AM	12/10/24 5:00 PM	16
20		use case diagram	2 days	12/6/24 8:00 AM	12/9/24 5:00 PM	16
21		activity diagram	3 days	12/6/24 8:00 AM	12/10/24 5:00 PM	16
22		Database Design	0 days	12/5/24 5:00 PM	12/5/24 5:00 PM	16


Fig:1

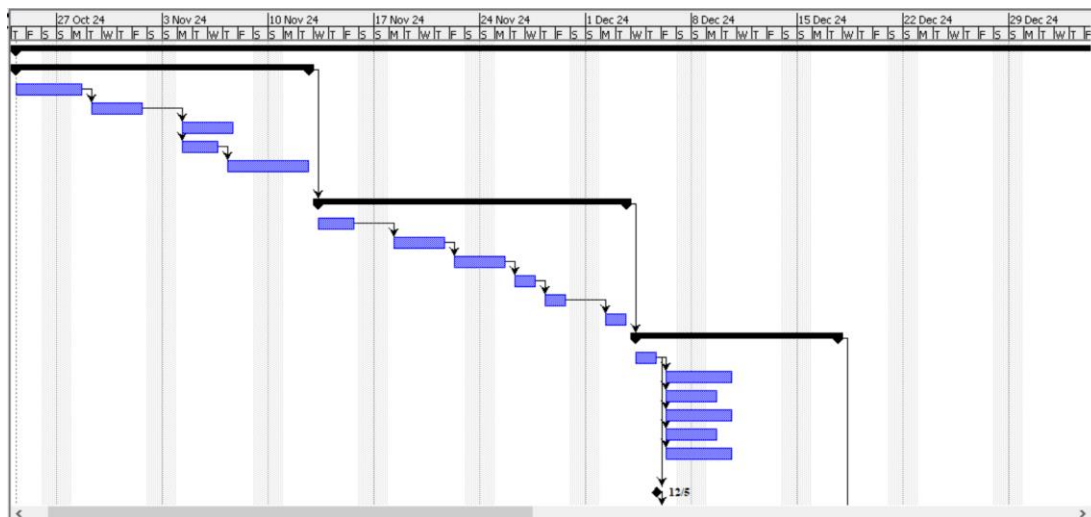

(this timeline chart is from fig-1 line(1-22))

	🔍	Name	Duration	Start	Finish	Pr
23		API Design	0 days	12/5/24 5:00 PM	12/5/24 5:00 PM	22
24		UI/UX Design	3 days	12/6/24 8:00 AM	12/10/24 5:00 PM	23
25		Design Login and Signup F	2 days	12/11/24 8:00 AM	12/12/24 5:00 PM	24
26		Design Dashboard	3 days	12/11/24 8:00 AM	12/13/24 5:00 PM	24
27		Design Meeting Creation I	5 days	12/11/24 8:00 AM	12/17/24 5:00 PM	24
28		Design Assignment Submi	3 days	12/11/24 8:00 AM	12/13/24 5:00 PM	24
29		Design Chat and Call Fea	3 days	12/11/24 8:00 AM	12/13/24 5:00 PM	24
30		Design Calendar and Sett	2 days	12/11/24 8:00 AM	12/12/24 5:00 PM	24
31	📅	📁Development	12 days	12/18/24 8:00 AM	1/2/25 5:00 PM	15
32		Frontend Development	1 day	12/18/24 8:00 AM	12/18/24 5:00 PM	
33		Implement Login and Sign	2 days	12/19/24 8:00 AM	12/20/24 5:00 PM	32
34		Develop Dashboard UI	3 days	12/23/24 8:00 AM	12/25/24 5:00 PM	33
35		Implement Meeting Creat	2 days	12/23/24 8:00 AM	12/24/24 5:00 PM	33
36		Develop Chat and Call Fe	4 days	12/26/24 8:00 AM	12/31/24 5:00 PM	34
37		Build Assignment and Exa	2 days	1/1/25 8:00 AM	1/2/25 5:00 PM	36
38		Backend Development	1 day	12/19/24 8:00 AM	12/19/24 5:00 PM	32
39		Develop Authentication S	3 days	12/20/24 8:00 AM	12/24/24 5:00 PM	38
40		Implement API for Assign	0 days	12/24/24 5:00 PM	12/24/24 5:00 PM	39
41		Build Meeting Managemer	3 days	12/25/24 8:00 AM	12/27/24 5:00 PM	40
42		Integrate Notification Sys	2 days	12/30/24 8:00 AM	12/31/24 5:00 PM	41
43		Database Integration	1 day	12/20/24 8:00 AM	12/20/24 5:00 PM	38


Fig:2

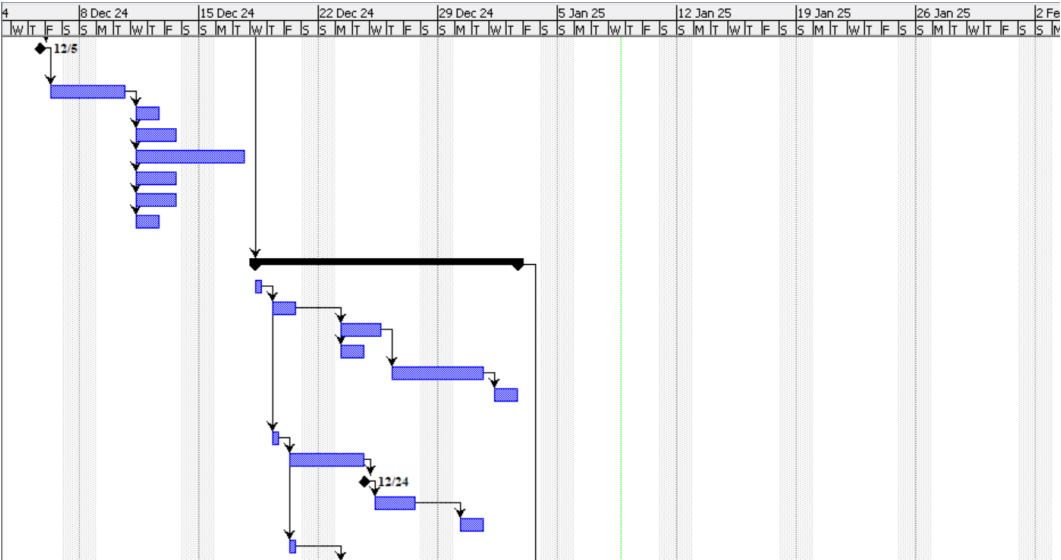


(this timeline chart is from fig-2 line(23-43))

		Name	Duration	Start	Finish	Predecessors
44		Setup User Database	2 days	12/23/24 8:00 AM	12/24/24 5:00 PM	43
45		Add Assignment and Exam	2 days	12/25/24 8:00 AM	12/26/24 5:00 PM	44
46		Configure Chat History S	0 days	12/26/24 5:00 PM	12/26/24 5:00 PM	45
47		Testing	8 days	1/3/25 5:00 PM	1/15/25 5:00 PM	31
48		Conduct Unit Testing	0 days	1/3/25 5:00 PM	1/3/25 5:00 PM	
49		System Testing	2 days	1/6/25 8:00 AM	1/7/25 5:00 PM	48
50		Resolve Bugs and Issues	0 days	1/7/25 5:00 PM	1/7/25 5:00 PM	49
51		Security Testing	0 days	1/7/25 5:00 PM	1/7/25 5:00 PM	50
52		Perform User Acceptance	0 days	1/7/25 5:00 PM	1/7/25 5:00 PM	51
53		Develop Test Cases	1 day	1/8/25 8:00 AM	1/8/25 5:00 PM	52
54		Login/Signup Test Cases	4 days	1/9/25 8:00 AM	1/14/25 5:00 PM	53
55		Meeting Creation Test Ca	3 days	1/9/25 8:00 AM	1/13/25 5:00 PM	53
56		Assignment Submission Te	4 days	1/9/25 8:00 AM	1/14/25 5:00 PM	53
57		Exam Attendance Test Ca	2 days	1/9/25 8:00 AM	1/10/25 5:00 PM	53
58		Chat and Call Features Te	5 days	1/9/25 8:00 AM	1/15/25 5:00 PM	53
59		Deployment	9 days	1/16/25 5:00 PM	1/29/25 5:00 PM	47
60		Setup Hosting Environmen	0 days	1/16/25 5:00 PM	1/16/25 5:00 PM	
61		Deploy Backend Services	3 days	1/17/25 8:00 AM	1/21/25 5:00 PM	60
62		Deploy Frontend Applicat	6 days	1/22/25 8:00 AM	1/29/25 5:00 PM	61
63		Configure Domain and SS	0 days	1/29/25 5:00 PM	1/29/25 5:00 PM	62
64		Launch Platform	0 days	1/29/25 5:00 PM	1/29/25 5:00 PM	63

Fig:3

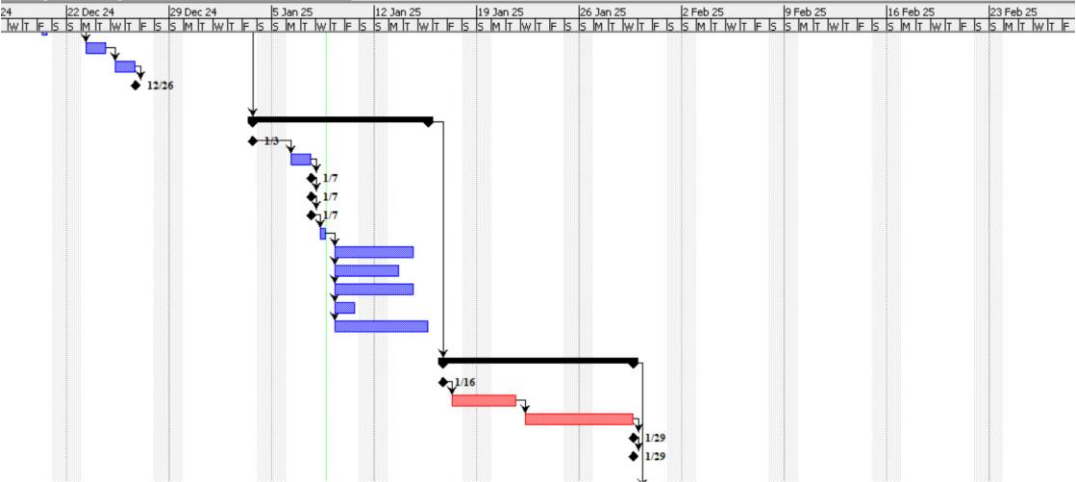

(this timeline chart is from fig-3 line(44-64))

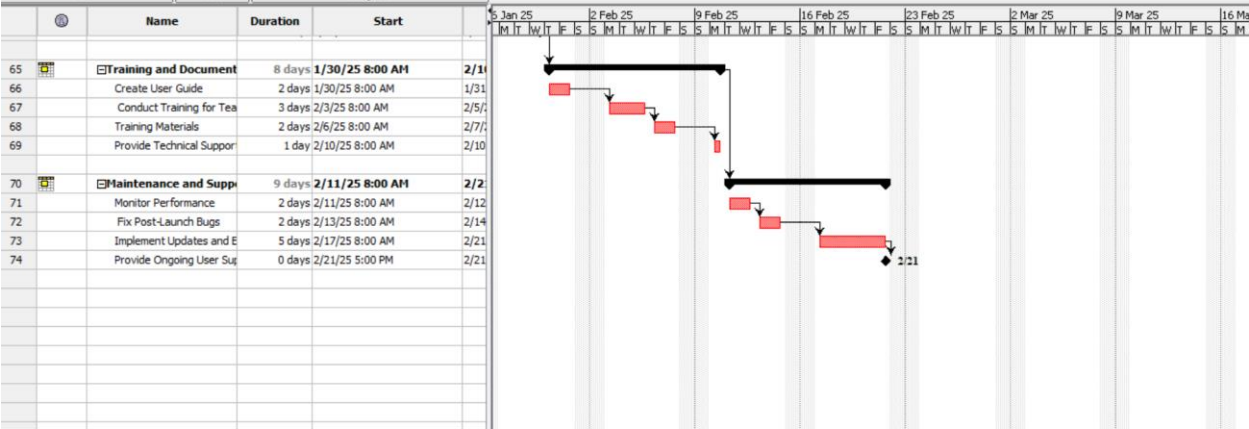

(this timeline chart is from line(65-74))
